Lofthus frukt og saft

Plan Start 4/11/2019

Plan ends 6/12/2019

ID	Depends on			DAYS
P001	T001	Planning		
T001		Client Meeting	Project Manager	1d
T002	T001	Dev Planning	Project Manager	1d
T003	T001	Staff Meeting	ALL	1d
T004	T002	Sketch Wireframe	Graphic Design	1d
T005	T009	Mid Project meeting	Project Manager	1d
T006	T014	Show finished product	Project Manager	1d
P002	T008	Development		
		Style Profile	Graphic Design	5d
T008	T004	HTML & CSS	Developer	7d
T009	T008	Back-end Dev	Developer	5d
T010	T008	Newsletter	Project Manager	2d
T011	T009	User interface	Developer	4d
T012	T001	Product photos	Photographer	5d
T013	T009	Testing	Out source	2d
T014	T013	Fixing bug reports	Developer	3d
P003	T014	Delivery week		

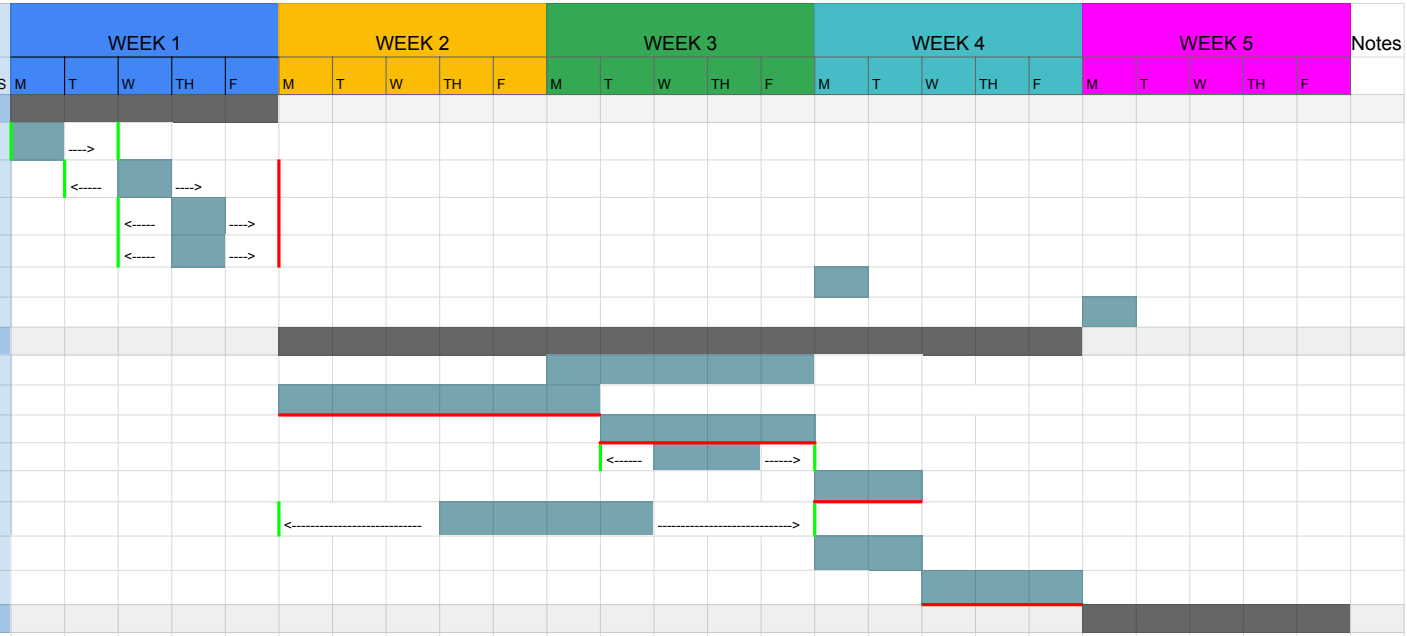

KEY information	Employees	Total time
Task Blocks = 1 work day	Project Manager	7d
Start and finish float	Developer	19d
Tasks must be finished	Graphic Design	6d
Critical path	Photographer	4d
